Masterlab Consortium For Engineering Consultations
Consultant Engineer
Dr. / Ahmed Fathy Abdelaziz & partners
Emeritus professor Faculty of Engineering Ain Shams University
Structural Engineering Department

Master-Lab

اتحاد ماسترلاب للاستشارات الهندسية
المهندس الاستشاري
دكتور / احمد فتحي عبد العزيز وشركاه
الاستاذ المتفرغ بكلية الهندسة جامعة عين شمس
قسم الهندسة الانشائية

Report (1) on Pull-out of:

MECHANICAL STEEL ANCHORS FIXED IN

Mockup Masonry Wall Constructed with DELTA BLOCKS

Project:
ICITY NEW CAIRO- Middle Radial Road.
آي سيتي التجمع – الطريق الدائري الاوسطي

Contractor: REDCON

Consultant: MB محرم/باخوم

Submitted to: DELTA BUILDING SYSTEMS

February 12, 2020

Authored by: Masterlab (Dr. Ahmed Fathy Abdel-Aziz)

Masterlab Consortium
For Eugineering Consultations
Dr. Eng. / Ahmed Fathy Abdelaziz
Syndicate : 361 / 6 Consultant : 2260 / 1 Record: 499 / 51

رقم (١) شارع البطراوي – مدينة نصر اول – شقة ١٠٣ – الدور الاول – القاهرة محمول : ٠١٠٠٢١٩٠٠٥٣
(1) El-Batrawi St., Nasr City 1st zone.Apartment 103 .1st floor - cairo Mob, : 01002190053 Email : masterlab2019@gmail.com

Masterlab Consortium For Engineering Consultations
Consultant Engineer
Dr. / Ahmed Fathy Abdelaziz & partners
Emeritus professor Faculty of Engineering Ain Shams University
Structural Engineering Department

Master-Lab

اتحاد ماسترلاب للاستشارات الهندسية
المهندس الاستشاري
دكتور / احمد فتحي عبد العزيز وشركاه
الاستاذ المتفرغ بكلية الهندسة جامعة عين شمس
قسم الهندسة الانشائية

Report (1) on Pull Out of:

STEEL ANCHOR BOLTS FIXED IN
Masonry Wall Constructed with Delta Blocks

Sample Specifications

Upon the request of **"DELTA BUILDING SYSTEMS."**, Pull out tests were performed at site on 16 steel mechanical anchor bolts 10& 12 mm diameter, fixed in mockup masonry wall at I City Project, NEW CAIRO- Middle Radial Road –in site. Samples were fixed by "FISHER", according to the designated data and on its sole responsibility. Tests were made as Destructive/Proof test to provide assurance that tested anchors will support an identified load which specified by the contractor, and to determine the structural response under this definite loading.

The methods used – within – include the application of these standard test methods and codes: BS 5080-1:1974 Methods of test for structural fixings in concrete and masonry. Tensile loading. BS 8539:2012 Code of Practice for the selection and installation of post-installed anchors in concrete and masonry. : E 488 – 96 Standard Test Methods for Strength of Anchors in Concrete and Masonry Elements.

Installation Details and Test Objectives

16 Mechanical Anchor bolts 10& 12 mm diameters, were fixed horizontally in mockup masonry wall constructed with solid blocks "Delta Blocks produced by Dela Building Systems- see attached catalogues". Anchor bolts were installed by client in accordance with the manufacturer's installation instructions or method statement. Drilling diameter and embedment depth were applied as specified respectively.

Masterlab Consortium
For Eugineering Consultations
Dr. Eng. / Ahmed Fathy Abdelaziz
Syndicate : 36176 Consultant : 2260 / 1 Record: 499 / 51

رقم (١) شارع البطراوي – مدينة نصر اول – شقة ١٠٣ – الدور الاول – القاهرة محمول : ٠١٠٠٢١٩٠٠٥٣
(1) El-Batrawi St., Nasr City 1st zone.Apartment 103 .1st floor - cairo Mob, : 01002190053 Email : masterlab2019@gmail.com

Base Material and Test location:

Anchor samples were fixed horizontally in mockup masonry wall constructed with solid blocks "Delta Blocks produced by Delta Building Systems- see attached catalogues" as described in test results - at random locations.

Attendance:

Tests were performed in the presence of:
Eng. Ahmed Elewa, Eng. Malaak Maximos, Eng. Islam Mabrouk, Eng. Amro Eldesouki, Eng. Basant Khaled, Eng. Ahmed Zeinhom, Eng. Esaam Sami

Represent **Delta Building Systems**

Eng.Khaled Ahmed — Represents Testing Agent

Test Equipment:

Tensile tests (Pull-Out) were performed on site 12/2/2020 for the tested samples, using Model 2050 tester with quick release hydraulic coupler of 0-50 kN pull-out load range of ± 0.5 % Accuracy (Photo-1). Samples were loaded gradually until failure, or loading was stopped at a specified certain safe load (Proof test load). Then, the maximum reached load or failure mode was registered. Testing system consists of: Load spreading bridge with three telescopic legs, Adjusting steel plates with different thicknesses, hollow rigid base plate, threaded stud adaptor M10& M12 and detachable 50kN digital gauge (Photo-1).

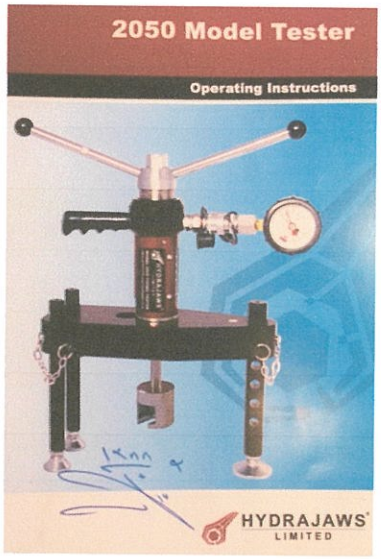

Photo 1. Testing device

Masterlab Consortium
For Eugineering Consultations
Dr. Eng. / Ahmed Fathy Abdelaziz
Syndicate : 361 / 6 Consultant : 2260 / 1 Record: 499 / 51

رقم (١) شارع البطراوي - مدينة نصر اول - شقة ١٠٣ - الدور الاول - القاهرة محمول : ٠١٠٠٢١٩٠٠٥٣
(1) El-Batrawi St., Nasr City 1st zone.Apartment 103 .1st floor - cairo Mob, : 01002190053 Email : masterlab2019@gmail.com

Test Results:

a) **Pull-out tests**

Test No.	Anchor Type	Diameter (mm)	Hole diameter (mm)	Embedded depth (mm)	Base Material	Floor	Maximum load (kN)	Failure Notes
1	FISHER FUR 10x100SSk	10	10	80	Delta Block Masonry Wall	H^{L} at Mockup Masonry Wall	1.2	Slipping
2							1.2	Slipping
3	**FISHER F10M152k**	10	10	130			**0.9**	**Slipping**
4							**1.1**	**Slipping**
5	FISHER UX10x60k	10	10	50			1.4	Slipping
6							0.9	Slipping
7	FISHER 58 Gk	10	10	40			1.4	Slipping
8							1.2	Slipping
9	FISHER GB 8k	10	10	40			2.8	Slipping
10							2.1	Slipping
11	FISHER M132k	10	10	100			0.8	Slipping
12							1.1	Slipping
13	FISHER EAM12N	12	14	40			0.6	Slipping
14							1.3	Slipping
15	Locally produced "Shield"	12	16	50			1.9	Slipping
16							1.9	Slipping

Tested by

Ahmed Hassan.

Revised by

Eng. Khaled Ahmed

Authorized By:
Consulting Engineer
DR./ AHMED FATHY ABDEL-AZIZ

Faculty of Engineering
Ain Shams University.
Structural Department

Masterlab Consortium
For Eugineering Consultations
Dr. Eng. / Ahmed Fathy Abdelaziz
Syndicate 3176 Consultant : 2260 / 1 Record: 499 / 51

Report 1 on Pull-Out Tests on: 12 February 2020

رقم (١) شارع البطراوي - مدينة نصر اول - شقة ١٠٣ - الدور الاول - القاهرة محمول : ٠١٠٠٢١٩٠٠٥٣
(1) El-Batrawi St., Nasr City 1st zone.Apartment 103 .1st floor - cairo Mob, : 01002190053 Email : masterlab2019@gmail.com
